



Project: WIS Project Date: Fri 05/10/07	Critical		Baseline		Project Summary	
	Critical Split		Baseline Split		External Tasks	
	Critical Progress		Baseline Milestone		External Milestone	
	Task		Milestone		Deadline	
	Split		Summary Progress			
	Task Progress		Summary			

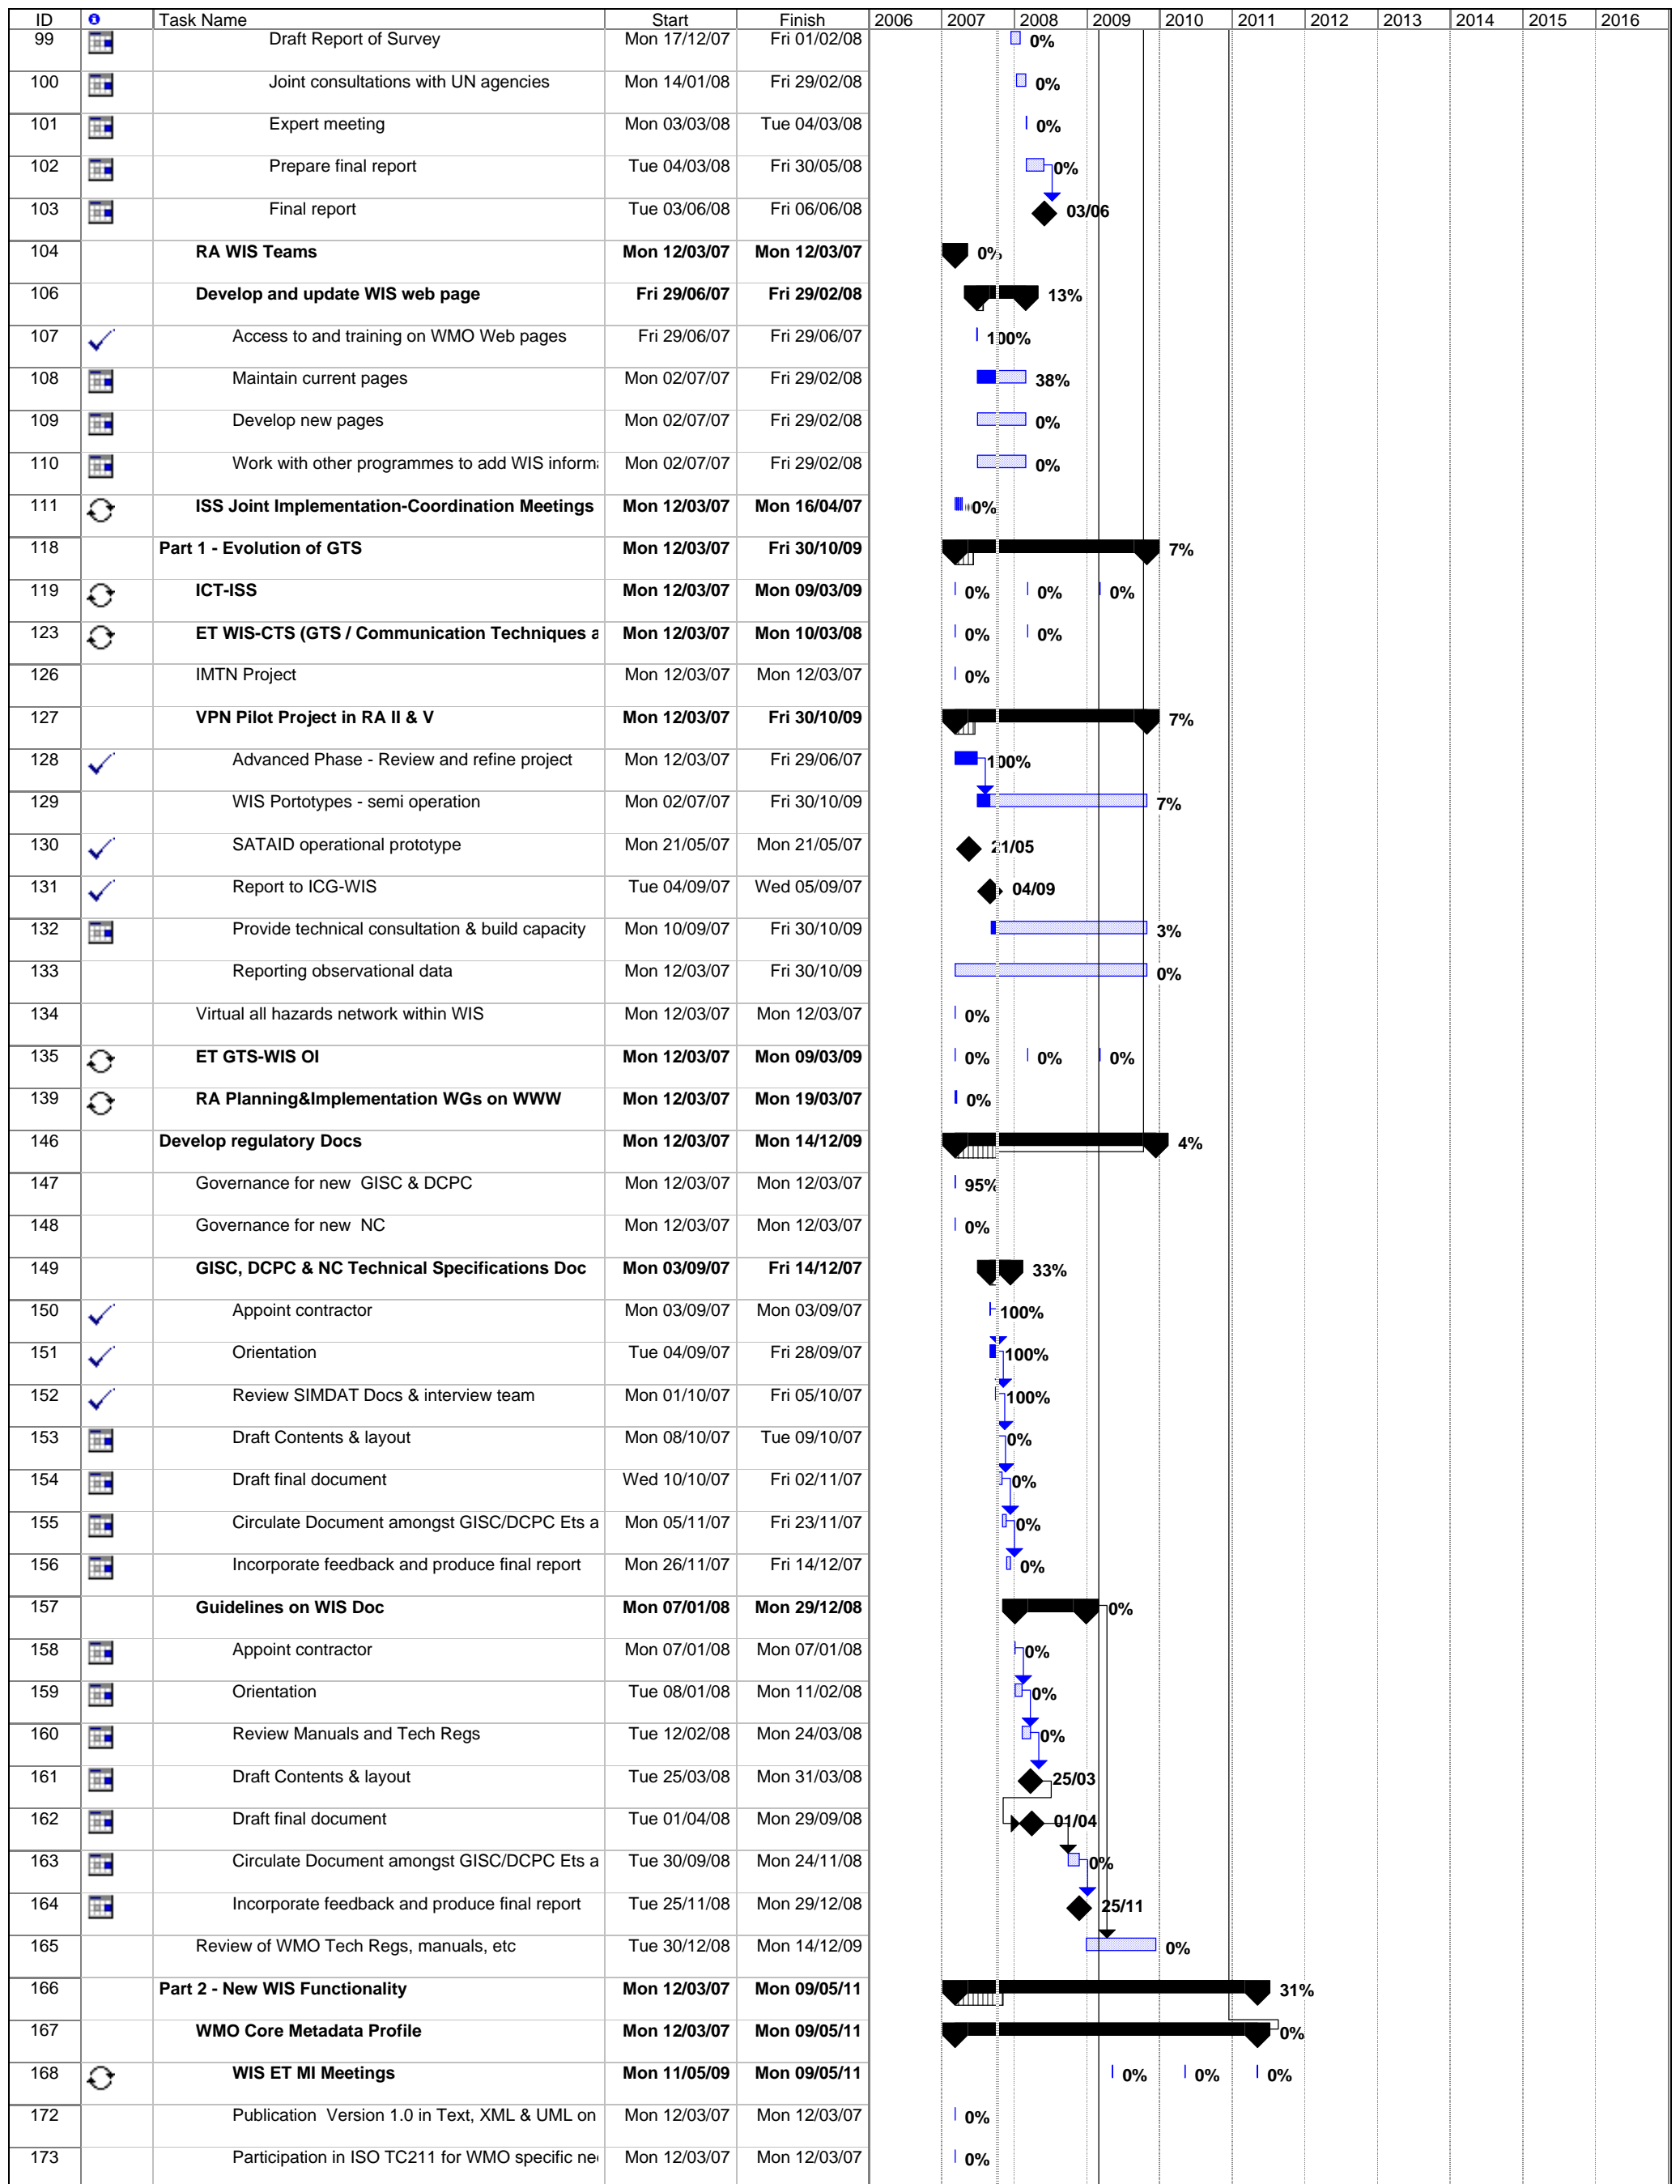

Project: WIS Project
Date: Fri 05/10/07

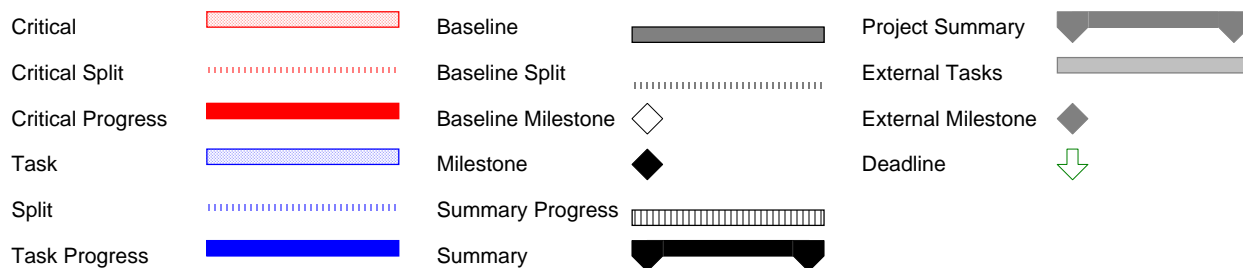

ID	Task Name	Start	Finish	2006	2007	2008	2009	2010	2011	2012	2013	2014	2015	2016
174	Development of Version 2	Mon 12/03/07	Mon 12/03/07		0%									
175	Metadata harvesting of routine data	Mon 12/03/07	Mon 12/03/07		0%									
176	Metadata Entry Tool	Mon 12/03/07	Mon 12/03/07		0%									
177	Metadata for station history etc	Mon 12/03/07	Mon 12/03/07		0%									
178	Capacity building and training	Mon 12/03/07	Mon 12/03/07		0%									
179	UNGIWG (UN Geospatial Information Working Group)	Mon 12/03/07	Mon 12/03/07		0%									
181	Develop & Implement GISC	Mon 12/03/07	Fri 01/05/09		32%									
182	Develop Security Procedures	Mon 31/12/07	Mon 31/12/07		0%									
183	European VGISC Region VI	Mon 12/03/07	Fri 01/05/09		32%									
184	Meetings	Wed 14/03/07	Fri 13/07/07		100%									
190	SIMDAT software development	Mon 12/03/07	Mon 31/03/08		70%									
191	Invitation to tender (ITT)	Mon 07/01/08	Fri 08/02/08		0%									
192	Tender evaluation	Mon 11/02/08	Fri 21/03/08		0%									
193	Build VGISC applications, test & install	Mon 24/03/08	Fri 19/09/08		0%									
194	Run VGISC in pseudo operational mode	Mon 22/09/08	Fri 01/05/09		0%									
195	EC endorsement of VGISC	Mon 30/06/08	Mon 30/06/08		0%									
196	Develop and Implement DCPC	Mon 12/03/07	Mon 12/03/07		0%									
197	UNIDART	Mon 12/03/07	Mon 12/03/07		0%									
198	NCAR DCPC	Mon 12/03/07	Mon 12/03/07		0%									
199	TIGGE	Mon 12/03/07	Mon 12/03/07		0%									
200	GAWSIS	Mon 12/03/07	Mon 12/03/07		0%									
201	WAMIS	Mon 12/03/07	Mon 12/03/07		0%									
202	CliWare	Mon 12/03/07	Mon 12/03/07		0%									
203	E2EDM Project	Mon 12/03/07	Mon 12/03/07		0%									
204	Develop & Implement WIS components of an NC	Mon 12/03/07	Mon 12/03/07		0%									
205	ET-WISC (Expert Team on WIS GISC & DCPC)	Mon 12/03/07	Wed 12/03/08		50%									
206	Meetings	Mon 12/03/07	Wed 12/03/08		100%	0%								
209	Capacity building and training	Mon 12/03/07	Mon 12/03/07		0%									
210	GISC	Mon 12/03/07	Mon 12/03/07		0%									
211	DCPC	Mon 12/03/07	Mon 12/03/07		0%									
212	NC	Mon 12/03/07	Mon 12/03/07		0%									
213	External users	Mon 12/03/07	Mon 12/03/07		0%									
214	Coordination with IGDDS	Mon 12/03/07	Mon 12/03/07		0%									
215	IGDDS compliance with WIS standards	Mon 12/03/07	Mon 12/03/07		0%									
216	IGDDS Implementation WG	Mon 12/03/07	Mon 12/03/07		0%									
217	Coordination with WIGOS	Mon 12/03/07	Mon 12/03/07		0%									
218	Meetings	Mon 12/03/07	Mon 12/03/07		0%									
219	Pilot Projects	Mon 12/03/07	Mon 12/03/07		0%									
220	JCOMM/WIS/WIGOS Interoperability Pilot Project	Mon 12/03/07	Mon 12/03/07		0%									
221	Interoperability with GEO	Mon 12/03/07	Fri 28/09/07		18%									
222	WIS (AR-07-04) WMO contribution to GEOSS	Mon 14/05/07	Thu 13/09/07		50%									
223	Meetings	Mon 14/05/07	Thu 13/09/07		100%									
226	WIS contribution to AR-07-01	Wed 28/03/07	Fri 28/09/07		89%									
227	Meetings	Wed 28/03/07	Fri 28/09/07		100%									
237	IP3 Scenario Development	Tue 20/03/07	Fri 31/08/07		0%									
238	GEO Component & Service Registry	Mon 12/03/07	Mon 12/03/07		0%									
239	GEO Service Standards registry	Mon 12/03/07	Mon 12/03/07		0%									
240	WIS Contribution to AR-07-02	Mon 12/03/07	Tue 25/09/07		94%									
241	Meetings	Tue 20/03/07	Tue 25/09/07		100%									
258	CFP	Mon 12/03/07	Mon 12/03/07		0%									

Project: WIS Project
Date: Fri 05/10/07

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			
