

ID	Task Name	Start	Finish	2007	2008	2009	2010	2011	2012	2013	2014	2015	
1	Project Management	Mon 3/12/07	Fri 5/22/15										26
2	Implementation Milestones	Fri 6/1/07	Wed 1/1/14										0%
3	Consolidate WIS plan	Fri 8/1/08	Fri 8/1/08			8/1							
4	Establish WMO Metadata Profile	Wed 10/1/08	Wed 10/1/08			10/1							
5	Develop Regulatory Documents	Fri 4/2/10	Fri 4/2/10				4/2						
6	Inclusion of WIS into IGDDS IP	Fri 6/1/07	Fri 6/1/07	6/1									
7	Implement First Operational GISC & DCPC	Mon 12/14/09	Mon 12/14/09				12/14						
8	Implement other operational GISCs	Thu 12/31/09	Thu 12/29/11				12/31						
9	Implement other DCPCs	Fri 1/1/10	Wed 1/1/14				1/1						
10	Congress Meetings	Mon 5/7/07	Fri 5/22/15										
14	Executive Council Meetings	Mon 3/26/07	Wed 4/1/15										
24	CBS	Mon 6/18/07	Wed 8/15/12										
31	ICG-WIS Meetings	Mon 9/3/07	Fri 7/19/13										
32	ICG WIS 4th Session (Reading)	Mon 9/3/07	Fri 9/7/07	9/3									
33	ICG WIS 5th Session (Brasillia)	Mon 7/14/08	Fri 7/18/08		7/14								
34	ICG WIS ad hoc Session (Geneva)	Mon 1/19/09	Fri 1/23/09			1/19							
35	ICG WIS 6th Session (Korea)	Mon 7/13/09	Fri 7/17/09			7/13							
36	ICG WIS 7th Session	Mon 7/5/10	Fri 7/9/10				7/5						
37	ICG WIS 8th Session	Mon 7/11/11	Fri 7/15/11					7/11					
38	ICG WIS 9th Session	Mon 7/9/12	Fri 7/13/12						7/9				
39	ICG WIS 10th Session	Mon 7/15/13	Fri 7/19/13							7/15			
40	EC WG WIGOS/WIS	Mon 12/3/07	Wed 11/5/14										
49	Project Manager Orientation	Mon 3/12/07	Fri 7/13/07	100%									
50	Consolidate WIS Plans (Proj & Imp Plan)	Mon 3/12/07	Thu 7/31/08										100%
51	Identify scope and project plan	Mon 3/12/07	Fri 5/11/07	100%									
52	Obtain background material	Mon 3/19/07	Fri 6/1/07	100%									
53	Develop Project Plan	Mon 5/7/07	Mon 6/4/07	100%									
54	Seek & incorporate Input from components	Mon 6/11/07	Mon 7/2/07	100%									
55	D/WWW to review plan	Tue 7/3/07	Mon 7/9/07	100%									
56	Incorporate D/WWW & other feedback	Tue 7/10/07	Fri 7/20/07	100%									
57	Add implementation plan	Mon 7/23/07	Fri 8/17/07	100%									
58	Review by WWW and WIS STC	Mon 8/20/07	Fri 8/24/07	100%									
59	Incorporate Feedback	Mon 8/27/07	Thu 8/30/07	100%									
60	Present to ICG-WIS	Fri 8/31/07	Fri 9/7/07		8/31								
61	Incorporate Feedback from ICG-WIS	Mon 9/10/07	Fri 9/28/07	100%									
62	Publish DRAFT Project Plan and Implementation Plan on WIS	Mon 10/1/07	Mon 10/1/07		10/1								
63	Log, review and incorporate feedback from Members	Tue 10/2/07	Mon 2/11/08			100%							
64	Prepare & Report on Plan to EC LX	Tue 2/12/08	Mon 3/31/08			100%							
65	Incorporate feedback from EC LX and replace DRAFT on WIS	Tue 4/1/08	Fri 4/4/08			100%							
66	Incorporate feedback from ICG-WIS and move from draft to ve	Mon 7/14/08	Thu 7/31/08				7/14						
67	WIS Secretariat Technical Committee (WIS STC)	Mon 3/19/07	Mon 7/30/07										99%
68	Meet Directors, Chiefs and Secretariat staff of Operational proç	Mon 3/19/07	Fri 6/1/07	100%									
69	Seek nominations for contact points	Mon 6/4/07	Fri 6/15/07	100%									
70	Meet contacts	Mon 6/18/07	Fri 7/27/07	100%									
71	Establish working practices under rearranged secretariat	Mon 7/30/07	Mon 7/30/07	0%									
72	Ad hoc travel (Meetings)	Mon 7/9/07	Mon 7/9/07										
73	DWD meeting with Stefan Mildner	Mon 7/9/07	Mon 7/9/07		7/9								
74	Outreach	Thu 4/12/07	Wed 9/2/09										51%
75	Presentations	Thu 4/12/07	Tue 9/30/08										
76	AREP (Geneva)	Thu 4/12/07	Thu 4/12/07		4/12								
77	JCOMM SOT (Geneva)	Fri 4/20/07	Fri 4/20/07		4/20								
78	JSC for CAS OPAG on WWRP (Geneva)	Mon 4/23/07	Mon 4/23/07		4/23								
79	JCOMM OCG (Geneva)	Mon 4/23/07	Mon 4/23/07		4/23								
80	HMIE on Metadata (Geneva)	Wed 5/9/07	Wed 5/9/07		5/9								
81	WIS side Congress side meeting (Geneva)	Tue 5/15/07	Tue 5/15/07		5/15								
82	Hydro & Water resources (Geneva)	Wed 8/1/07	Wed 8/1/07		8/1								
83	WMO Training Programme (Geneva)	Tue 8/14/07	Tue 8/14/07		8/14								
84	DRR Expert Meeting (Geneva)	Mon 11/26/07	Tue 11/27/07			11/26							
85	GEMS Bureau (Geneva)	Tue 12/18/07	Tue 12/18/07			12/18							
86	WCP/CCI meeting on RCPs (Geneva)	Mon 1/21/08	Mon 1/21/08			1/21							
87	GEMS Architecture Meeting (Brussels)	Tue 1/22/08	Tue 1/22/08			1/22							
88	IPY ITG meeting (Geneva)	Fri 1/25/08	Fri 1/25/08			1/25							
89	DRR Tsunami meeting (Geneva) jmr	Wed 2/27/08	Wed 2/27/08			2/27							
90	JCOMM DMCG (Oostende)	Wed 3/26/08	Fri 3/28/08			3/26							
91	GAW/WIGOS (Geneva)	Tue 3/25/08	Tue 3/25/08			3/25							
92	SeaDataNet (Athens)	Thu 4/3/08	Fri 4/4/08			4/3							
93	AMDAR/WIGOS (Geneva)	Wed 7/2/08	Thu 7/3/08			7/2							


Project: WIS Project
Date: Thu 4/30/09

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			


ID	Task Name	Start	Finish	2007	2008	2009	2010	2011	2012	2013	2014	2015
94	IPY Data Mgt Meeting (Russia)	Mon 7/7/08	Tue 7/8/08		7/7							
95	ECOMET (Oslo) - Hoffman	Thu 7/10/08	Thu 7/10/08		7/10							
96	GMDS meeting - Henri Savina	Mon 8/25/08	Mon 8/25/08		8/25							
97	TIGGE/THORPEX meeting -Geneva	Mon 9/22/08	Mon 9/22/08		9/22							
98	WCRP - WOAP (Colorado) - Middleton	Tue 9/30/08	Tue 9/30/08		9/30							
99	WIS Rolling Review of Requirements	Mon 5/14/07	Tue 3/31/09	78%								
100	Congress Side Meeting	Mon 5/14/07	Mon 5/14/07	5/14								
101	Orientation	Mon 5/14/07	Mon 6/11/07	100%								
102	Interviews	Mon 5/28/07	Mon 7/16/07	100%								
103	Prepare & report to ICG-WIS	Mon 8/13/07	Fri 9/7/07	100%								
104	Appoint contractor	Mon 9/3/07	Mon 9/3/07	100%								
105	Report Preparation	Tue 9/4/07	Fri 12/21/07	100%								
106	Draft layout & Content	Tue 9/4/07	Fri 10/26/07	100%								
107	Incorporate post ICG-WIS feedback	Mon 10/29/07	Fri 11/16/07	100%								
108	Initial Draft report	Mon 11/19/07	Fri 12/7/07	100%								
109	release Draft Report (Ver 0.3)	Mon 12/10/07	Fri 12/21/07	100%								
110	Report review	Wed 1/2/08	Mon 3/9/09	50%								
111	Incorporate feedback from ECWG WIGOS/WIS	Wed 1/2/08	Fri 3/21/08	100%								
112	Programmes verification of content	Mon 3/24/08	Thu 5/1/08	0%								
113	Review by selected implementors (ET-OI& ET-CTS)	Fri 5/2/08	Wed 5/21/08	0%								
114	Incorporate feedback and reviews	Thu 5/22/08	Wed 6/11/08	0%								
115	Present to ICG-WIS 2008	Mon 7/14/08	Mon 7/14/08	100%								
116	Report to CBS 2009	Mon 3/9/09	Mon 3/9/09	0%								
117	Implementation of RRR	Tue 3/31/09	Tue 3/31/09	0%								
118	Set up ET etc (TBD)	Tue 3/10/09	Tue 3/10/09	0%								
119	Identification of potential users of WIS	Mon 7/16/07	Fri 9/19/08	8%								
120	DRR - International Organisations (ISDR, FAO, UNOCHA)	Mon 7/16/07	Fri 9/19/08	8%								
121	Develop a project plan	Mon 7/16/07	Fri 7/27/07	100%								
122	Develop Survey	Fri 2/1/08	Tue 3/4/08	48%								
123	Distribute Survey & Collect responses	Wed 3/5/08	Tue 4/22/08	0%								
124	One on one interviews	Wed 4/23/08	Tue 6/17/08	0%								
125	Draft Report of Survey	Wed 6/18/08	Tue 8/5/08	0%								
126	Joint consultations with UN agencies	Thu 5/1/08	Thu 7/31/08	0%								
127	Expert meeting	Mon 3/3/08	Tue 3/4/08	0%								
128	Prepare final report	Wed 6/18/08	Mon 9/15/08	0%								
129	Final report	Tue 9/16/08	Fri 9/19/08	9/13								
130	RA WIS Teams	Thu 11/29/07	Tue 12/30/08	0%								
131	RA I	Thu 11/29/07	Tue 12/30/08	0%								
132	VPN Pilot Project	Thu 11/29/07	Tue 12/30/08	0%								
133	Develop and update WIS web page	Fri 6/29/07	Wed 9/2/09	70%								
134	Access to and training on WMO Web pages	Fri 6/29/07	Fri 6/29/07	100%								
135	Maintain current pages	Mon 7/2/07	Fri 11/28/08	89%								
136	Develop new pages	Tue 7/1/08	Fri 7/31/09	100%								
137	Work with other programmes to add WIS information	Fri 8/1/08	Wed 9/2/09	15%								
138	ISS Joint Implementation-Coordination Meetings	Mon 11/26/07	Tue 11/27/07	11/26								
139	I&C Meeting IMTN Cloud I	Mon 11/26/07	Tue 11/27/07	11/26								
140	Part A - Evolution of GTS	Mon 3/12/07	Fri 12/30/11	61%								
141	Current GTS implementation	Mon 3/12/07	Fri 12/30/11	95%								
142	ICT-ISS	Mon 3/12/07	Mon 3/9/09									
146	ET WIS-CTS (GTS / Communication Techniques and Structure)	Mon 5/26/08	Fri 5/30/08	100%								
147	ET-CTS (Toulouse)	Mon 5/26/08	Fri 5/30/08	100%								
148	IMTN Project	Mon 3/12/07	Mon 3/12/07	0%								
149	VPN Pilot Project in RA II & V	Mon 3/12/07	Fri 10/30/09	39%								
150	Initial phase	Mon 3/12/07	Mon 3/12/07	100%								
151	Advanced Phase - Review and refine project	Mon 3/12/07	Fri 6/29/07	100%								
152	WIS Prototypes - semi operation	Mon 7/2/07	Fri 10/30/09	54%								
153	SATAID operational prototype	Mon 5/21/07	Mon 5/21/07	5/21								
154	Report to ICG-WIS	Tue 9/4/07	Wed 9/5/07	9/4								
155	Provide technical consultation & build capacity	Mon 9/10/07	Fri 10/30/09	61%								
156	Reporting observational data	Mon 3/12/07	Fri 10/30/09	0%								
157	Virtual all hazards network within WIS	Mon 3/12/07	Mon 3/12/07	0%								
158	ET GTS-WIS OI	Tue 9/23/08	Fri 9/26/08	9/23								
159	ET GTS-WIS OI (Geneva)	Tue 9/23/08	Fri 9/26/08	9/23								
160	RA Planning&Implementation WGs on WWW	Mon 3/26/07	Tue 8/25/09									
161	P&I WG on WWW RA I	Mon 3/10/08	Mon 3/10/08	3/10								
162	WG on P&I of WWW Region II	Mon 9/10/07	Wed 9/12/07	9/10								
163	P&I WG on WWW RA III	Mon 1/5/09	Mon 1/5/09	1/5								

Project: WIS Project
Date: Thu 4/30/09

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			

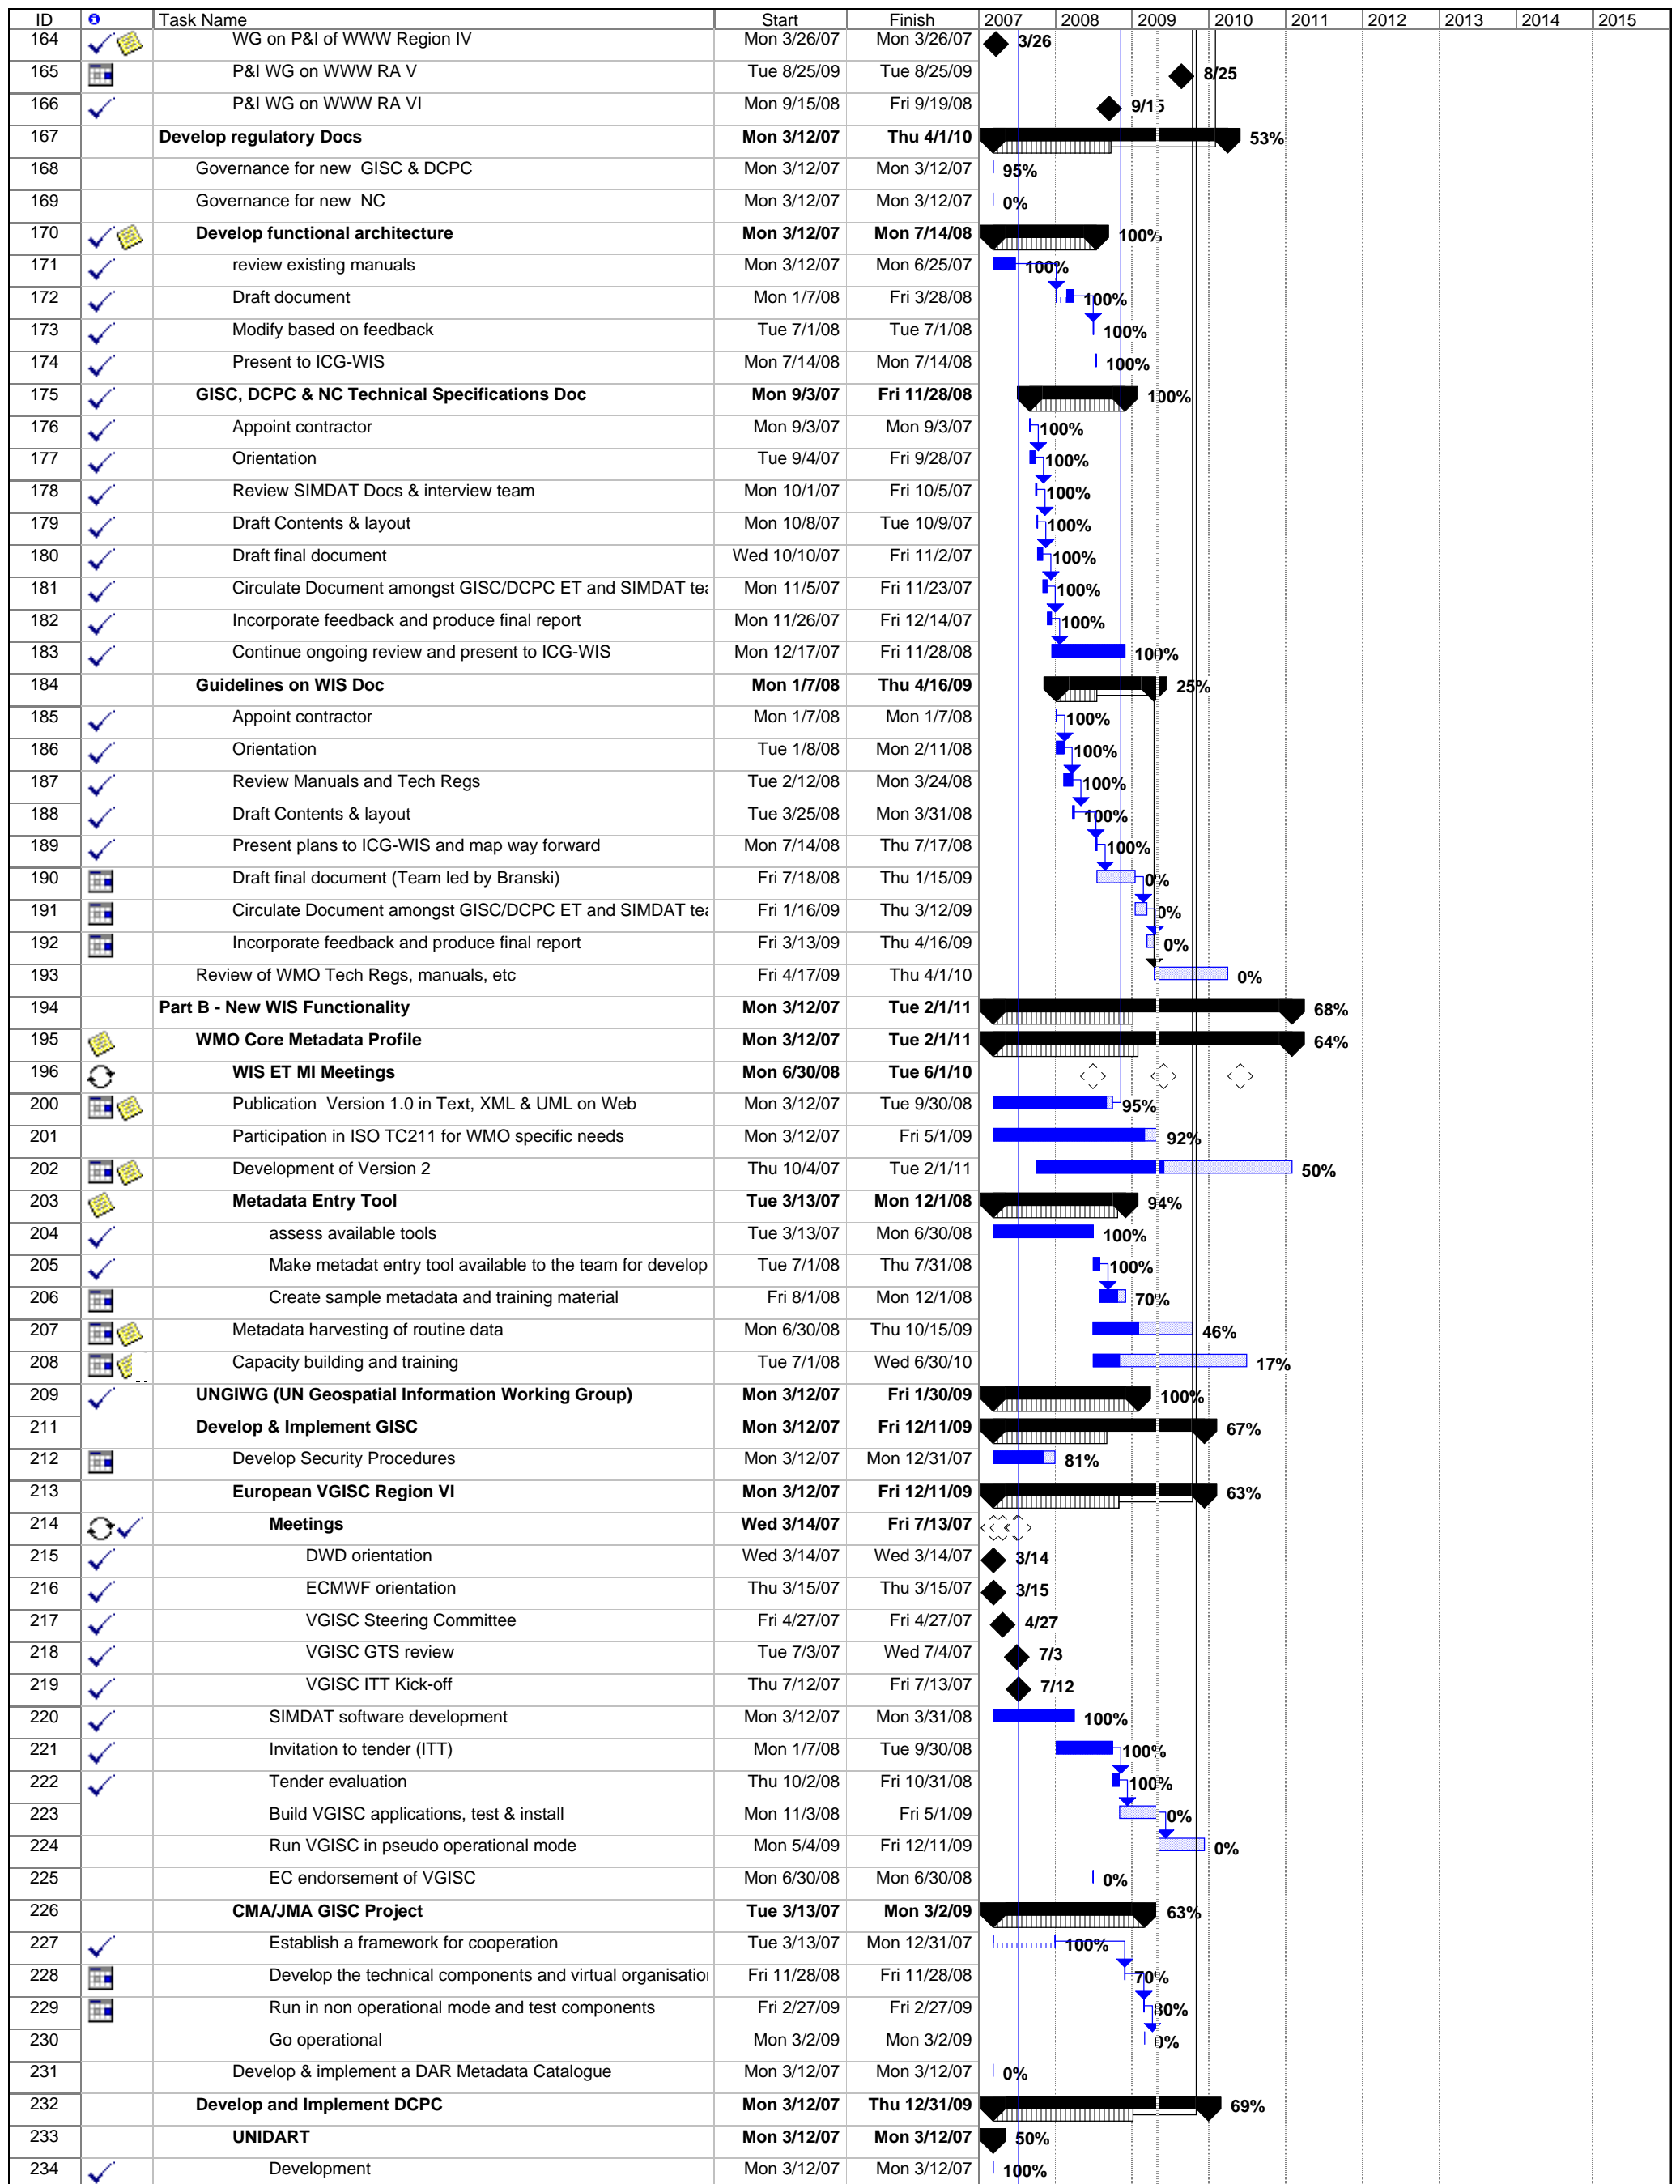

Project: WIS Project
Date: Thu 4/30/09

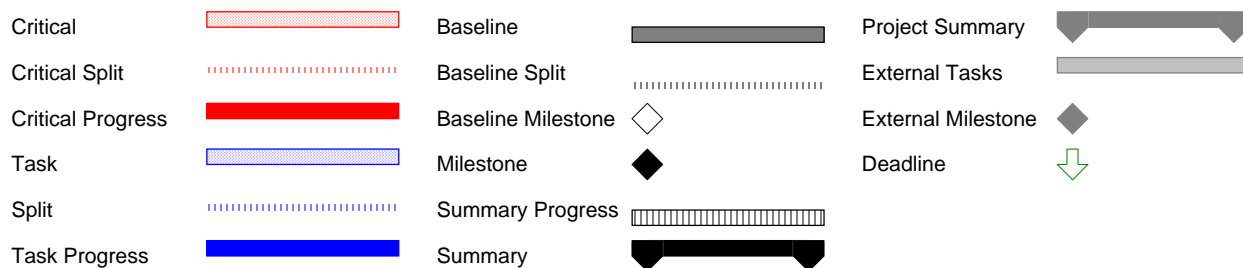

ID	Task Name	Start	Finish	2007	2008	2009	2010	2011	2012	2013	2014	2015
235	Implementation within Climate Programme & IPY	Mon 3/12/07	Mon 3/12/07	0%								
236	NCAR DCPC	Mon 3/12/07	Mon 3/12/07	0%								
237	TIGGE	Mon 3/12/07	Mon 3/12/07	0%								
238	GAWSIS	Mon 3/12/07	Mon 3/12/07	0%								
239	WAMIS	Mon 3/12/07	Mon 3/12/07	0%								
240	CliWare	Mon 3/12/07	Wed 12/31/08									
241	Pilot Project	Mon 3/12/07	Mon 3/12/07	100%								
242	Roll out of system across Federated States	Mon 3/12/07	Wed 12/31/08									
243												
244	Climsoft Data and Metadata interface development	Mon 5/5/08	Fri 12/25/09									
245	Phase 1 - evaluate systems and standards	Mon 5/5/08	Fri 10/3/08									
246	Phase 2- Climsoft workshop & followup	Mon 10/6/08	Wed 12/31/08									
247	Phase 3 - develop e-learning module	Mon 1/5/09	Fri 12/25/09									
248	E2EDM Project	Mon 3/12/07	Thu 12/31/09									
249	Pilot Project	Mon 3/12/07	Mon 3/12/07	100%								
250	Implement in other Ocean Data Centres	Mon 3/12/07	Thu 12/31/09									
251	Develop & Implement WIS components of an NC	Mon 3/12/07	Mon 3/12/07	20%								
252	ET-WISC (Expert Team on WIS GISC & DCPC)	Mon 3/12/07	Fri 6/13/08									
256	Capacity building and training	Mon 3/12/07	Mon 3/12/07									
261	Coordination with IGDDS	Mon 3/12/07	Fri 1/29/10									
262	Inclusion of WIS into IGDDS plan	Mon 3/12/07	Fri 6/1/07	100%								
263	IGDDS compliance with WIS standards	Wed 8/1/07	Wed 12/2/09									
264	Catalogue & metadata (partial)	Wed 8/1/07	Fri 5/30/08									
265	Catalogue and metadata (full implementation)	Mon 6/2/08	Wed 12/2/09									
266	IGDDS Data RRR	Mon 3/12/07	Thu 12/31/09									
267	IGDDS Data Requirements (initial)	Mon 3/12/07	Mon 6/30/08									
268	IGDDS RRR (ongoing)	Tue 7/1/08	Thu 12/31/09									
269	RARS Data exchange	Mon 3/12/07	Fri 5/30/08									
270	Europe	Mon 3/12/07	Fri 5/30/08									
271	Europe (core)	Mon 3/12/07	Fri 6/1/07	100%								
272	Extension into Indian Ocean	Mon 8/6/07	Fri 5/30/08									
273	Asia-Pacific	Mon 3/12/07	Fri 5/30/08									
274	South America	Mon 3/12/07	Fri 5/30/08									
275	Data exchange (China-Europe)	Mon 3/12/07	Mon 12/31/07									
276	DVB-S Dissemination	Mon 3/12/07	Fri 1/29/10									
277	EUMETCAST (Europe-Africa)	Mon 3/12/07	Fri 11/28/08									
278	FengYunCast (Asia-Pacific)	Mon 3/12/07	Fri 10/31/08									
279	Americas	Mon 3/12/07	Fri 1/29/10									
280	IGDDS Implementation WG	Thu 7/5/07	Tue 7/7/09									
281	Session 1	Thu 7/5/07	Fri 7/6/07									
282	Session 2	Thu 5/22/08	Fri 5/23/08									
283	Session 3	Mon 7/6/09	Tue 7/7/09									
284	Coordination with WIGOS	Fri 9/28/07	Fri 12/31/10									
285	Preparatory work	Fri 9/28/07	Fri 9/28/07	100%								
286	Pilot Projects	Mon 3/24/08	Fri 12/31/10									
287	JCOMM-IODE/WIS/WIGOS Interoperability Pilot Project	Mon 3/24/08	Fri 12/31/10									
288	AMDAR WIGOS PP (Metadata & BUFR)	Wed 7/2/08	Thu 12/31/09									
289	GAW WIGOS PP	Tue 3/25/08	Fri 12/31/10									
290	Interoperability with GEO	Mon 3/12/07	Fri 11/28/08									
291	WIS (AR-07-04) WMO contribution to GEOSS	Mon 5/14/07	Tue 9/23/08									
292	Meetings	Mon 5/14/07	Tue 9/23/08									
293	ADC 4th meeting (Tokyo)	Mon 5/14/07	Tue 5/15/07									
294	ADC 5th meeting (Washington DC)	Wed 9/12/07	Thu 9/13/07									
295	ADC 6th meeting (Italy)	Wed 2/6/08	Thu 2/7/08									
296	ADC 7th meeting (Geneva)	Tue 5/20/08	Tue 5/20/08									
297	ADC 8th meeting (Boulder -IEEE)	Mon 9/22/08	Tue 9/23/08									
298	WIS contribution to AR-07-01	Wed 3/28/07	Fri 9/28/07									
299	Meetings	Wed 3/28/07	Fri 9/28/07									
309	IP3 Scenario Development	Tue 3/13/07	Fri 11/28/08									
310	Develop and report on IP3 scenarios	Tue 3/13/07	Fri 11/30/07									
311	Extend IP3 scenarios and explore new opportunities	Mon 1/7/08	Fri 11/28/08									
312	GEO Component & Service Registry	Mon 3/12/07	Mon 3/12/07	80%								
313	GEO Service Standards registry	Mon 3/12/07	Mon 3/12/07	80%								
314	WIS Contribution to AR-07-02	Mon 3/12/07	Tue 9/25/07									
315	Meetings	Tue 3/20/07	Tue 9/25/07									
332	CFP	Mon 3/12/07	Mon 3/12/07	50%								

Project: WIS Project
Date: Thu 4/30/09

Critical		Baseline		Project Summary	
Critical Split		Baseline Split		External Tasks	
Critical Progress		Baseline Milestone		External Milestone	
Task		Milestone		Deadline	
Split		Summary Progress			
Task Progress		Summary			
